



## **CHEROKEE COUNTY ROADWAY CAPITAL PROGRAM MANAGEMENT**

### **PROJECT STATUS REPORT**

**July 31, 2023**

# CONSTRUCTION STATUS MONTHLY REPORT

JULY 2023

| No. | Project No. | Project Name  | Description   | Contractor                          | Notice to Proceed | Contract Days | Estimated Completion Date | Current Contract Amount | Earned to Date  | % Complete | Status  |
|-----|-------------|---|---|-------------------------------------|-------------------|---------------|---------------------------|-------------------------|-----------------|------------|---|
| 1   | 72106       | Wiley Bridge Road at Cox Road                         | Roundabout  | Colditz Trucking                    | 3/15/2022         | 270           | 7/28/2023                 | \$ 929,635.48           | \$ 745,983.53   | 80.2%      | Final Accepted 7/28/2023  |
| 2   | 75708       | 2023 Resurfacing Project                              | Paving various roads in Cherokee County   | Bartow Paving Company, Inc.         | 4/3/2023          | 120           | 7/31/2023                 | \$ 3,254,655.50         | \$ 3,013,066.00 | 92.6%      | Contractor complete with paving. Need punchlist and thermo striping completed.  |
| 3   | 72110       | Union Hill Road at Lower Union Hill Road              | Roundabout  | Ohmshiv Construction                | 2/13/2023         | 180           | 8/11/2023                 | \$ 1,936,636.36         | \$ 528,582.85   | 27.3%      | Roundabout opened on 7/31. Contractor to work on remaining items. Offsite drainage plan revision forthcoming.   |
| 4   | 73118       | Etowah Valley Estates                                 | Drainage Repairs  | RDJE, Inc.                          | 2/27/2023         | 183           | 8/28/2023                 | \$ 916,219.00           | \$ 460,740.50   | 50.3%      | Contractor to be completed by August. Change Order forthcoming for structure inverts.   |
| 5   | 72118       | SR 140 at Scott Road and Avery Road                   | Intersection Improvement  | Wilson Construction Management, LLC | 1/16/2023         | 180           | 9/14/2023                 | \$ 831,497.83           | \$ 258,114.01   | 31.0%      | Construction began on Avery Rd installing right and left turn lanes.  |
| 6   | 72121       | Kellogg Creek Road at Jacobs Road                     | Lower vertical curve at intersection with Jacobs Road   | Baldwin Paving Company, Inc.        | 1/23/2023         | 180           | 9/21/2023                 | \$ 767,616.88           | \$ 368,193.84   | 48.0%      | Road Open 7/26. Contractor to complete punchlist and additional drainage work needed.   |
| 7   | 73114       | Rhine Road  | Roadway Improvement Project from SR 20 to Upper Sweetwater Trail                                  | Bartow Paving Company, Inc.         | 1/2/2023          | 270           | 9/28/2023                 | \$ 2,747,862.71         | \$ 1,599,711.97 | 58.2%      | Asphalt to be completed week of 7/31 base and binder. Contractor to begin final dressing entire project. Final layer of asphalt to follow.  |
| 8   | 73098       | Shoal Creek Culvert Replacement                       | Culvert replacement and road re-alignment   | JG Leone Enterprises, Inc.          | 4/10/2023         | 180           | 10/6/2023                 | \$ 1,765,716.95         | \$ 277,327.74   | 15.7%      | Excavation almost complete for new re-alignment of Shoal Creek Road. Darters in creek restricted until Army Corp Permit is re-newed. US Fish & Wildlife is reviewing. Hembree Water relocation to begin soon. |
| 9   | 72125       | East Cherokee Drive at SR 140 Walls                   | Stone façade on retaining walls   | SH Creel Contracting                | 7/10/2023         | 90            | 10/7/2023                 | \$ 117,820.00           | \$ -            | 0.0%       | Stone Façade progressing as planned should be complete by end of August.  |
| 10  | TBD         | Hunter Trail at Bells Ferry Rd                        | Intersection Improvement  | Bartow Paving Company, Inc.         | 6/12/2023         | 120           | 10/9/2023                 | \$ 379,971.77           | \$ -            | 0.00%      | Road base installed. CCWSA relocating waterline. Curb and asphalt to follow.  |
| 11  | 73035       | Hames Road  | Roadway Reconstruction - SR 92 to Jamerson Road; includes roundabout at S. Jett Road intersection | Bartow Paving Company, Inc.         | 6/15/2022         | 545           | 12/11/2023                | \$ 5,028,160.19         | \$ 1,540,890.57 | 30.6%      | Roundabout at Hames and Jett open for traffic to travel north to SR 92. Traffic at West Oaks Place/Trail to travel south towards Jamerson. Contractor working on Hames Rd to West Oaks Place/Trail.           |
| 12  | 73121       | Technology Ridge Parkway, Phase I                     | New Alignment Roadway   | CW Matthews                         | 10/31/2022        | 548           | 4/30/2024                 | \$ 9,091,709.17         | \$ 2,536,634.92 | 27.9%      | Clearing completed. Excavating Ponds 1, 2 and roadway and exporting dirt to Airport Expansion project. Utilities have begun relocating. Schedule shows beginning on Bluffs Pkwy roundabout in August.         |
| 13  | 74008       | Kingland St at N Briar Ridge Galfs Road at Rocky Lane | Drainage Improvement  | Vertical Earth, Inc.                | TBD               | 180           | TBD                       | \$ 888,920.84           | \$ -            | 0.0%       | BOC Award 8/1. Pre-Con to follow.   |
| 14  | 75710       | 2023 LMIG Safety Action Plan (SAP)                    | Striping on various roads   | TBD                                 | TBD               | TBD           | TBD                       | TBD                     | TBD             | TBD        | GDOT funding \$200,000.00 with 30% match from County to provide assistance for safety. County to stripe various roads. BOC 8/1.   |
| 15  | 73130       | City of Nelson Drainage Project Phase 3               | Drainage Project for City of Nelson   | TBD                                 | TBD               | TBD           | TBD                       | TBD                     | TBD             | TBD        | County to provide construction management and inspection services for the City of Nelson. Project funded 100% by City of Nelson.  |

| No. | Project No.            | Project   | Description  | Consultant/Designer                   | Phase              | Proposed Letting Date | Design / Pre-Construction Status  | R/W Parcels (closed/req'd) | Comments   |
|-----|------------------------|---|--|---------------------------------------|--------------------|-----------------------|---|----------------------------|--|
| 1   | 74008                  | Dupree Road and King Arthur Drive                 | Drainage Improvement Project   | American Engineers (AEI)              | Right-of-way       | 3rd Quarter 2023      | Project kickoff meeting held on 10/26/21. Concept plan received on 1/26/22. Preliminary plans approved. Right of way acquisition underway. Additional sidewalk added to project. Bid package is ready to go as soon as ROW is finished.                                     | 2/5                        | Drainage improvements to install piping and culverts to correct flooding issue.  |
| 2   | 72122                  | Ball Ground Highway Roundabout                    | Installation of a single-lane roundabout at the intersection of Ball Ground Highway and Howell Bridge Road | Southeastern Engineering, Inc. (SEI)  | Preliminary Design | 4th Quarter 2023      | Kickoff meeting held 11/7/22. Concept received. Preliminary design underway.  | TBD                        | Roundabout will be converted to a multi-lane roundabout as part of the Ball Ground Bypass.   |
| 3   | 73105                  | Hickory Road Sidewalks                            | Sidewalk and Intersection Improvement  | Volkert                               | Right-of-way       | 4th Quarter 2023      | Project extended to New Light Road. Concept for the project extension has been approved. In right of way acquisition. New plans expected, parcels may change.   | 10/13                      | Fill in the gap sidewalk project along Hickory Rd between SR 140 and East Cherokee Dr. East Cherokee Dr and Hickory Rd intersection to be brought up to ADA standards. Additional sidewalks to be added to Hickory Road and Stringer Road. |
| 4   | 71005 GDOT PI #0013525 | Bells Ferry Road over Little River/Lake Allatoona | Bridge Replacement Project   | VHB, Inc.                             | Right-of-way       | 2nd Quarter 2024      | Working with ACOE and marina owners regarding permitting needs and impacts to marina operations. Plans revised to accommodate new driveway location. Right of way has been authorized. Met with ACOE on 3/20/2023. Finalizing cost to cures and appraisals.                 | 0/1                        | GDOT design and construct. County to acquire right-of-way. GDOT working to bid with Bells Ferry Road project. County will look at possibility of advanced acquisition of restaurant parcel.  |
| 5   | 72100 GDOT PI #0016365 | Trickum Road at SR 92                             | Intersection Improvement Project   | Southeastern Engineering, Inc. (SEI)  | Right-of-way       | 4th Quarter 2024      | Right of way estimate complete. Utility relocation estimate complete. Concept Report has been submitted to GDOT. Utility coordination underway. Preliminary plans received. PFPR held on 10/28/21. ROW authorized and underway. FFPR held 2/16/23. Plan revisions underway. | 4/20                       | Intersection improvements project to include dual-left-turn lanes and receiving lanes on northbound and southbound Trickum Road approaches to SR 92. Also includes reconfiguration of Trickum Road at Gunnin Road intersection.            |
| 6   | 73115                  | South Jeff Road                                   | Roadway Improvement Project  | Atlas Technical Consultants           | Right-of-way       | 3rd Quarter 2024      | Kickoff meeting held 12/3/2020. Preliminary engineering approved. Right of way acquisition underway.  | 18/19                      | Realign South Jeff Road to remove severe curve and add sidewalk on the east side. Project to be coordinated with Hames Road  |
| 7   | 72115                  | SR 140 at Batesville Road/Hickory Road            | Intersection Improvement Project   | Heath & Lineback Engineers            | Right-of-way       | 4th Quarter 2024      | Initial traffic study submitted to GDOT. Review meeting held 12/15/2020. Revised plans have been received. Right of way acquisition underway  | 29/31                      | Intersection improvements project to include additional turn lanes and through lanes on all legs of the intersection.  |
| 8   | 73093                  | Trickum Road - Sycamore Lane to Belles Lane       | Installation of a center left-turn lane  | Arcadis                               | Final Design       | 4th Quarter 2024      | Right of way acquisition complete.  | 24/25                      | Roadway improvements include installation of a center left-turn lane for entire length and installation of sidewalk along the west side of the corridor.   |
| 9   | 74008                  | Mountain Park Road                                | Drainage Improvement Project   | Practical Design Partners             | Right-of-way       | TBD                   | Project in review. Test holes complete. Design complete. Right of way acquisition underway. Project will be revised per field visit.  | 3/5                        | Drainage improvements to pipe existing overland flow   |
| 10  | 63001 GDOT PI #0013526 | Bells Ferry Road - Southfork Way to Victoria Road | Widening from 2 to 4 lanes   | VHB, Inc.                             | Right-of-way       | TDB                   | Design is in progress. Utility coordination and storm drainage design being completed. Right of way acquisition in progress.  | 129/138                    | GDOT design and construct. County to acquire right-of-way. Project limit revised to end at Victoria Road. GDOT is proposing to use HB 170 funds for construction.  |
| 11  | 63089                  | S. Cherokee Lane                                  | Improve a substandard County roadway   | BM&K Construction & Engineering, Inc. | Right-of-way       | TBD                   | Right of way acquisition in progress. Consultant looking at changes to minimize some easement areas. Cherokee County will need to look at the last 2 parcels. Additional 1,800 linear feet added to the project. Revised ROW plans under review.                            | 25/28                      | Project includes improving horizontal and vertical alignment on 3,000 feet of substandard roadway.   |
| 12  | 74008                  | Water Tank Road at Canton Creek                   | Drainage Improvement Project   | Calco Engineering                     | Right-of-way       | TBD                   | Environmental screening complete. Preliminary plans complete. Right of way acquisition underway. USACE coordination to begin.   | 4/6                        | Drainage improvements to upgrade existing non-functional culverts  |
| 13  | 74008                  | Allatoona Pass at Woodstock Road                  | Drainage Improvement Project   | Calco Engineering                     | Right-of-way       | TBD                   | Concept approved 7/26/2022. Preliminary plans complete. Right of way acquisition underway   | 12/16                      | Drainage improvements in existing neighborhood to upgrade existing system  |
| 14  | 74008                  | Creekview Subdivision                             | Drainage Improvement Project   | Calco Engineering                     | Right-of-way       | TBD                   | Kickoff meeting held 9/7/22. Preliminary plans complete. Right of way acquisition underway. Utility coordination complete.  | 8/10                       | Drainage improvements in existing neighborhood to upgrade existing system  |
| 15  | 74008                  | Union Hill Road at Mill Creek Tributary           | Drainage Improvement Project   | Practical Design Partners             | Right-of-way       | TBD                   | Kickoff meeting held 4/27/22, preliminary plans complete  | TBD                        | Drainage improvements to upgrade existing non-functional culverts  |
| 16  | 72018                  | Sugar Pike & Batesville                           | Roundabout   | MaesAwy, LLC                          | Right-of-way       | TBD                   | Right-of-way acquisition in progress. Working on project revision due to right of way negotiations.   | 3/7                        | Intersection improvements that includes the installation of a roundabout   |

| No. | Project No.            | Project   | Description                       | Consultant/Designer                   | Phase              | Proposed Letting Date | Design / Pre-Construction Status   | R/W Parcels (closed/req'd) | Comments   |
|-----|------------------------|---|-----------------------------------|---------------------------------------|--------------------|-----------------------|--|----------------------------|--|
| 17  | 74008                  | Shaw Drive Culvert Replacement  | Drainage Improvement Project      | Southeastern Engineering, Inc. (SEI)  | Right-of-way       | TBD                   | Kickoff meeting held 2/1/22. Preliminary plans complete. Right of way acquisition underway.  | 0/2                        | Drainage improvements to replace existing undersized culvert   |
| 18  | 73128 GDOT PI #0002525 | Ball Ground Bypass  | New alignment roadway             | TBD                                   | Preliminary Design | TBD                   | Concept Report approved 10/22/21. Funding for PE awarded by ARC. PFA in for BOC approval and signature. RFQ being developed.   | TBD                        | New alignment roadway from SR 369 to SR 5.   |
| 19  | 72101 GDOT PI #0019631 | 575 at Towne Lake Parkway Interchange Operational Improvements (PI 0019361) | Interchange Improvement Project   | Arcadis                               | Preliminary Design | TBD                   | Concept Report has been approved by GDOT. Kickoff meeting held 5/10/23. Survey underway. Environmental studies underway  | TBD                        | Interchange improvement study to add capacity to the interstate ramps. Additional lanes added to Towne Lake Parkway.   |
| 20  | 72117 GDOT PI #0017804 | SR 140 at Univeter Road   | Intersection Improvement Project  | VHB, Inc.                             | Preliminary Design | TBD                   | Kickoff meeting held on August 12, 2021. Traffic and environmental studies complete. CTM held June 29, 2022. A3M held July 7, 2022. Anticipating Concept Report approval. PFPR plans under review. | TBD                        | Intersection improvements to include double left turns on to Univeter, widening of all approaches.   |
| 21  | 73122                  | Old Dawsonville Road  | Fill in the gap sidewalk project  | Practical Design Partners             | Preliminary Design | TBD                   | Concept approved May 2022. Survey complete. Design underway. Preliminary plans under review, ROW plans complete.   | TBD                        | Fill in the gap sidewalk project in the City of Ball Ground between William Court and Tom Avery Drive.   |
| 22  | 73123                  | Holbrook Campground Road at Midway Road                                     | Intersection Improvement Project  | Practical Design Partners             | Preliminary Design | TBD                   | Concept approved 6/20/22. Survey complete. Preliminary plans under review. Right of way plans being developed Comments sent 7/21/2023  | TBD                        | Intersection improvement project to improve skewed intersection.   |
| 23  | 73126                  | Old Alabama Road Sidewalks  | Fill in the gap sidewalk project  | BM&K Construction & Engineering, Inc. | Preliminary Design | TBD                   | Kickoff meeting held 9/18/22. Preliminary plans under review; comments sent 5/30/23  | TBD                        | 4,000 linear foot sidewalk addition  |
| 24  | 72111                  | East Cherokee Drive at Bradshaw Drive and Avery Creek Drive                 | Intersection Improvement Projects | Volkert                               | Preliminary Design | TBD                   | Kickoff meeting held 9/15/22. Survey underway. Preliminary plans under review.   | TBD                        | Intersection improvements to include additional left turn lanes and right turn lanes.  |
| 25  | PI 0019205. 73125      | Bells Ferry Multi-Use Trail   | Multi-Use Trail Project           | Thomas & Hutton                       | Preliminary Design | TBD                   | Project Framework Agreement approved. Project RFQ out for Phase 1 review complete. RFQ Phase 2 complete. GDOT kickoff meeting 6/20/2023. Environmental boundary being established.                 | TBD                        | Ten foot multi-use trail project from the Cobb County line to Victory Road.  |
| 26  | 73124                  | Bates Drive   | Sidewalk Project                  | Calco Engineering                     | Preliminary Design | TBD                   | Project awarded January 24, 2023; final plans received. ROW pending.   | TBD                        | Sidewalk connection project, including curb and gutter   |
| 27  | 74008                  | Stell Road  | Drainage Improvement Project      | Calco Engineering                     | Preliminary Design | TBD                   | Project awarded March 10, 2023; Kickoff meeting was March 20, 2023. Completed alignments and construction limits.  | TBD                        | Drainage improvements along substandard roadway  |
| 28  | 72124                  | Holly Springs Parkway at Palm Drive   | Intersection Improvement Project  | Keck & Wood                           | Preliminary Design | TBD                   | Project awarded March 22, 2023; Kickoff meeting on March 31, 2023; survey & concept layout underway  | TBD                        | Realign Palm Drive to create 4 way signalized intersection at River Park Boulevard   |
| 29  | 72123                  | East Cherokee Drive at Mill Creek Drive                                     | Roundabout                        | Keck & Wood                           | Preliminary Design | TBD                   | Project awarded April 4th. Kickoff meeting on April 12th. Concept being developed.   | TBD                        | Creation of a roundabout at the entrance to a new subdivision.   |
| 30  | 74008                  | Woodstock Road over Kellogg Creek   | Drainage Improvement Project      | Southeastern Engineering, Inc. (SEI)  | Concept            | TBD                   | Drainage study complete 8/2022. Concept to be determined, working to establish bridge type   | TBD                        | Drainage improvements to upgrade existing non-functional culverts  |
| 31  | 73088                  | Heard Road Extension/Technology Ridge Parkway                               | Scoping Study                     | VHB, Inc.                             | Concept            | TBD                   | Concept validation and surveys underway. Initial concept for Phase 4 and 5 reviewed. Preliminary alignment for Phase 2 and 3 complete. Plans for Phase 4 and 5 beginning.                          | N/A                        | Scoping study to determine project scope, schedule and budget. Determine path for potential roadway and right-of-way needs. Determine environmental permitting requirements and potential utility conflicts. |
| 32  | 73104                  | Hidden Branches   | Drainage project                  | Atlas Technical Consultants           | Reviewing          | TBD                   | Construction plans revised and complete. Right of way acquisition to be completed.   | 3/5                        | Replacement of deteriorating culverts  |
| 33  | 73110                  | Canton Street Extension   | Roadway Improvement Project       | Calco Engineering                     | On Hold            | TBD                   | Design complete. Right of way acquisition to be completed.   |                            | Upgrade of deficient roadway.  |
| 34  | 72096                  | SR 140 at Darnell Road  | Intersection Improvements         | BM&K Construction & Engineering, Inc. | On Hold            | TBD                   | Project design is complete.  | 0/6                        | Project includes adding left-turn lane from westbound SR 140 to Darnell Road.  |
| 35  | 72120                  | Damascus Road Intersections   | Intersection Improvement Project  | Calco Engineering                     | On Hold            | TBD                   | Kickoff meeting held 5/14/2021. Concept development approved. Preliminary plans approved. Right of way acquisition put on hold.  | 2/5                        | Intersection improvement projects at the intersections at Upper Bethany Road and Soap Creek Road   |



# PUBLIC WORKS 2023 PROJECTS STATUS MONTHLY REPORT

**JULY 2023**

| No. | Project Name                       | Description   | Beginning Point       | Ending Point       | Status  | Miles |
|-----|------------------------------------|---|-----------------------|--------------------|---|-------|
| 1   | White Road                         | Patch/Overlay; shoulder work  | Address 1274          | Bartow County Line | Complete April 2023                             | 1.284 |
| 2   | Mt. Olive Church Lane              | Patch/Overlay, leveling, shoulder work  | SR-20                 | White Road         | Complete April 2023                             | 0.938 |
| 3   | Clearwater Trail                   | Leveling/pave   | SR-20                 | Cul-de-sac         | Complete June 2023                              | 0.213 |
| 4   | Mt Carmel Church Lane              | Full Depth Reconstruction; shoulder work  | SR-108                | End of CO Maint    | Completed July 2023                             | 1.800 |
| 5   | Pea Ridge Community Center Parking | Pave parking lot  | N/A                   | N/A                | Need to demo building on Moore property         | N/A   |
| 6   | City of Waleska                    | City coordination working on a building site expansion, drainage and parking lot. | N/A                   | N/A                | Light clean up is all that remains to be done   | N/A   |
| 7   | Westridge Trace                    | Patch/Overlay   | Westland Mill Dr      | Address 6227       | Completed July 2023                             | 0.200 |
| 8   | Salacoa Road                       | Patch/Level/Overlay   | Jerusalem Church Road | Bartow County Line | Estimated completion middle of August 2023      | 3.992 |
| 9   | Yellow Creek Drive                 | Patch/Overlay   | SR-369                | Conns Creek Road   | Fall of 2023                                    | 5.170 |
| 10  | Kennesaw Ave                       | City of Nelson IGA Project  | Canton Highway        | City Limit Sign    | Estimated completion August of 2023             | 0.794 |
| 11  | Nelson Oaks Drive                  | City of Nelson IGA Project  | Old Nelson Road       | Cul-de-sac         | Estimated completion August of 2023             | 0.270 |
| 12  | Baker Street                       | City of Nelson IGA Project  | Kennesaw Ave.         | Canton Highway     | Estimated completion August of 2023             | 0.320 |
| 13  | Huey Barnes Lane                   | Construct road to County Standards  | Lower Burris Road     | End of CO Maint    | Scheduled to begin work week of August 14, 2023 | 0.401 |
| 14  | Large Court                        | Pave, cul-de-sac, and drainage  | Old Farm Road         | Dead End           | September 2023                                  | 0.100 |

# PUBLIC WORKS 2023 PROJECTS STATUS MONTHLY REPORT

**JULY 2023**


| No. | Project Name                | Description   | Beginning Point           | Ending Point                                  | Status   | Miles         |
|-----|-----------------------------|---|---------------------------|---|--|---------------|
| 15  | Brigham Circle              | Grind/Binder/Overlay  | Univeter Road             | Univeter Road                                 | Late Summer 2023   | 0.605         |
| 16  | Stacy Court                 | 2" Binder/Overlay   | Brigham Circle            | Cul-de-sac                                    | Binder has been applied, will top end of Summer 2023                                       | 0.326         |
| 17  | Peardon Court               | Patch/Overlay   | End of CO Maint           | End of CO Maint                               | Late Summer 2023   | 0.116         |
| 18  | Peardon Road                | Pave and widen to 18'; Extend existing cross pipe   | New Light Road            | Peardon Court                                 | Late Summer 2023   | 0.218         |
| 19  | Upper Sweetwater Trail      | Final project is Field Fit Widening   | SR-20                     | Campbell Trail                                | ROW & TCE Acquisition Underway; Leveling underway  | 2.183         |
| 20  | Rampley Trail               | Field Fit Widening  | Sam Nelson                | East of Patriot Trail to End of CO Maint      | Anticipate to begin clearing late fall of 2023   | 1.631         |
| 21  | Lula Payne Trail            | Widen, improve and resurface a substandard width roadway  | SR-372                    | End of CO Maint                               | Working with Sawnee EMC to assist in removal of trees along roadway. Reevaluating project. | 0.648         |
| 22  | Liberty Church Lane         | Roadway Improvement Project   | SR-372                    | End of CO Maint                               | ROW staked; evaluating project scope   | 0.534         |
| 23  | Haynes Lane                 | Pave-Widen with Asphalt   | Haynes Circle             | End of CO Maint                               | Evaluating Schedule  | 0.206         |
| 24  | Haynes Circle               | Pave-Widen with Asphalt   | Holly Street              | Haynes Circle/Gate                            | Evaluating Schedule  | 0.332         |
| 25  | Mountain Park Road          | Deep Patch Roots/Level/Overlay  | Wiley Bridge Road         | Fulton County Line                            | Scheduling with drainage project   | 0.605         |
| 26  | Steels Bridge Road Sidewalk | Sidewalk project connecting the end of the sidewalk from BridgeMill to end of Parc Steels Bridge Subd. For future connectivity to Bells Ferry | +/- 620 Steels Bridge Rd. | +/- 226 Steels Bridge Rd. (Across the street) | Had discussions with concrete contractor and has submitted cost for his scope of work      | N/A           |
| 27  | Jay Green Road              | Speed humps installed   | N/A                       | N/A   | Fall of 2023   | N/A           |
| 28  | Wrights Mill Road           | Speed humps installed   | N/A                       | N/A   | Fall of 2023   | N/A           |
| 29  | Owens Road                  | Speed humps installed   | N/A                       | N/A   | Fall of 2023   | N/A           |
|     |                             |   |                           |   | <b>TOTAL MILES</b>   | <b>21.837</b> |





**UNION HILL ROAD AT LOWER UNION HILL ROAD IMPROVEMENTS**



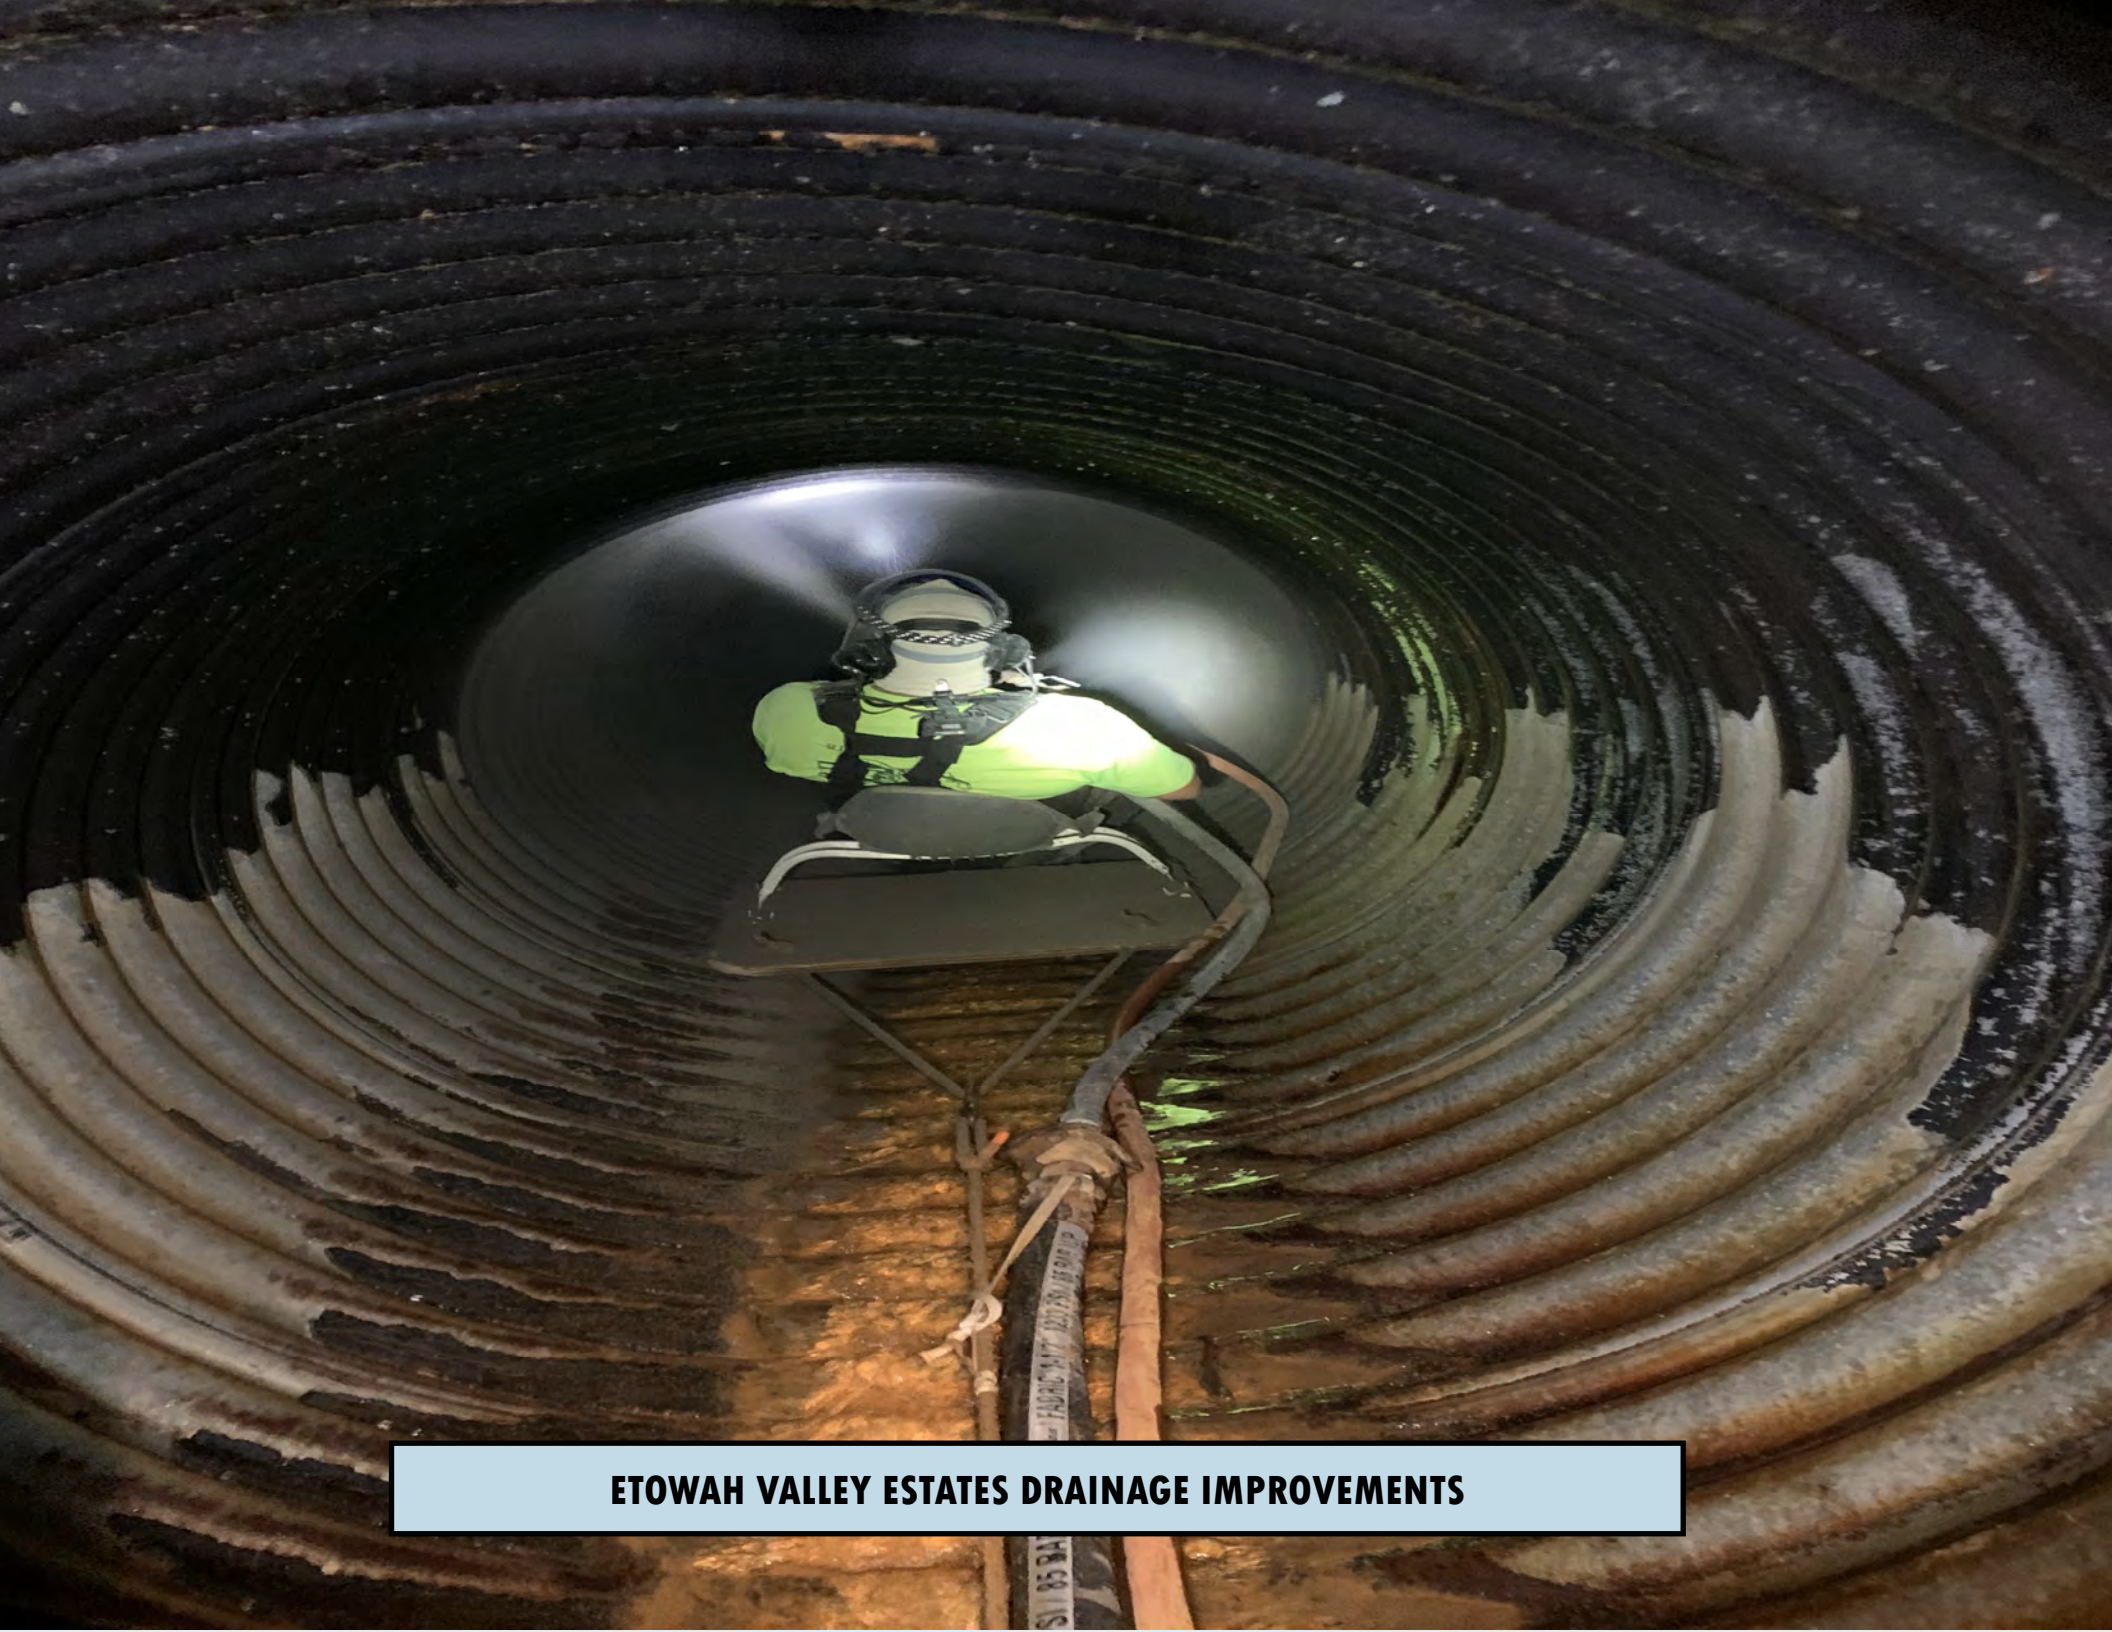

**ETOWAH VALLEY ESTATES DRAINAGE IMPROVEMENTS**





**SR 140 AT SCOTT ROAD AND AVERY ROAD INTERSECTION IMPROVEMENTS**





**KELLOGG CREEK ROAD AT JACOBS ROAD INTERSECTION IMPROVEMENT**





**RHINE ROAD IMPROVEMENTS**





**SHOAL CREEK ROAD BOX CULVERT REPLACEMENT**





**HAMES ROAD RECONSTRUCTION**





**TECHNOLOGY RIDGE PARKWAY NEW CONSTRUCTION**





**MT OLIVE CHURCH LANE IMPROVEMENTS**






CVS pharmacy

**EAST CHEROKEE DRIVE AT SR 140 STONE FAÇADE ON CONCRETE WALLS**





**WESTRIDGE TRACE**

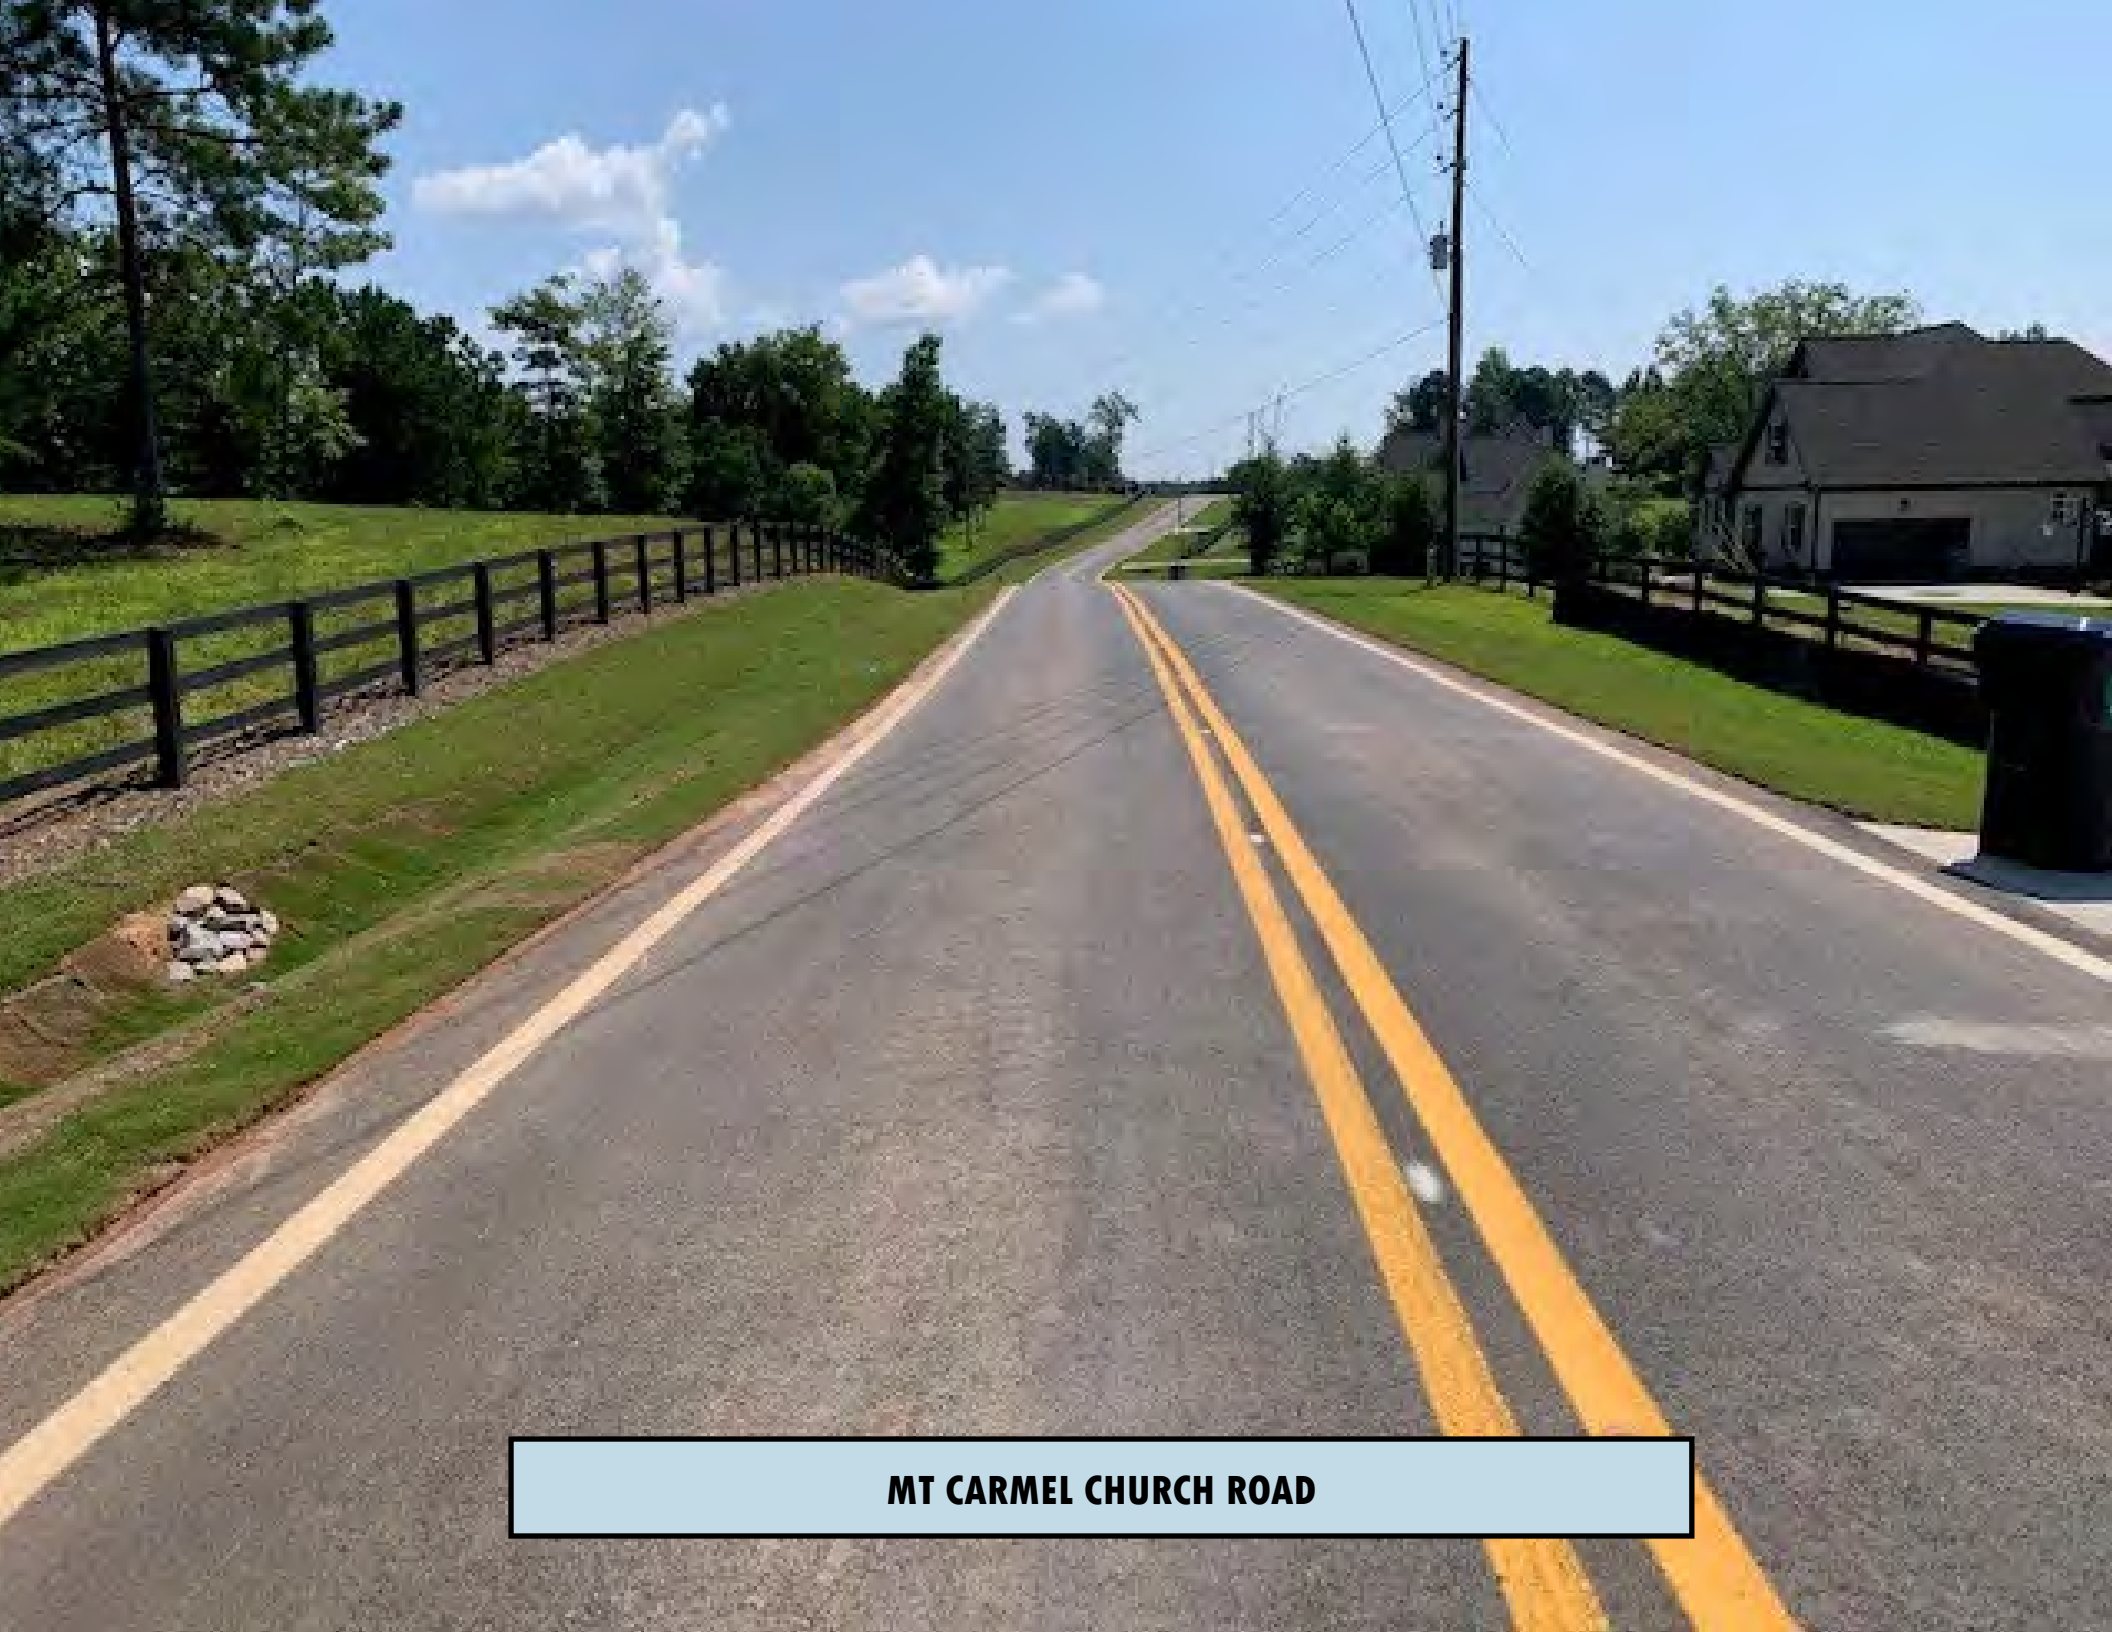

**MT CARMEL CHURCH ROAD**





**SALACOA ROAD**
